MARGAM CREMATORIUM - rev A - 12th March 2019

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		**2018/2019 Margam Crem extension**	**52 days**	**Mon 24/09/18**	**Tue 04/12/18**	
2		RIBA 0 - Strategic Definition	1 wk	Mon 24/09/18	Fri 28/09/18	
3		RIBA 1 - Preparation and Brief	1 wk	Mon 01/10/18	Fri 05/10/18	2
4		RIBA 2 - Concept Design	2 wks	Mon 08/10/18	Fri 19/10/18	3
5		RIBA 3 - Developed Design	4 wks	Mon 22/10/18	Fri 16/11/18	4
6		CADW	13 wks	Mon 07/01/19	Fri 05/04/19	
7		RIBA 4 - Detailed Design- Arch	52 days	Mon 19/11/18	Fri 08/02/19	5
8		RIBA 4 - Detailed Design - M+E	35 days	Mon 14/01/19	Fri 01/03/19	7SS
9		RIBA 4 - QS Tender prep	4 wks	Mon 11/02/19	Fri 08/03/19	8SS+3
10		RIBA 4 - Tender period	5 wks	Mon 11/03/19	Fri 12/04/19	9
11		RIBA 4 - Tender evaluation	2 wks	Mon 15/04/19	Fri 26/04/19	10
12		RIBA 5 - Mobilisation & (D+B early design if applicable)	2 wks	Mon 29/04/19	Fri 10/05/19	11,6
13		RIBA 5 - Construction phase	20 wks	Mon 13/05/19	Fri 27/09/19	12
14		RIBA 6 - Handover and PC issued	0 days	Fri 27/09/19	Fri 27/09/19	13
15						
16		**M+E Ventilation - Option 2A**	**175 days**	**Mon 07/01/19**	**Fri 06/09/19**	
17		Design	9 wks	Mon 07/01/19	Fri 08/03/19	
18		Tender negotiation and award	4 wks	Mon 11/03/19	Fri 05/04/19	17
19		Lead in	12 wks	Mon 08/04/19	Fri 28/06/19	18,6
20		Construction	10 wks	Mon 01/07/19	Fri 06/09/19	19

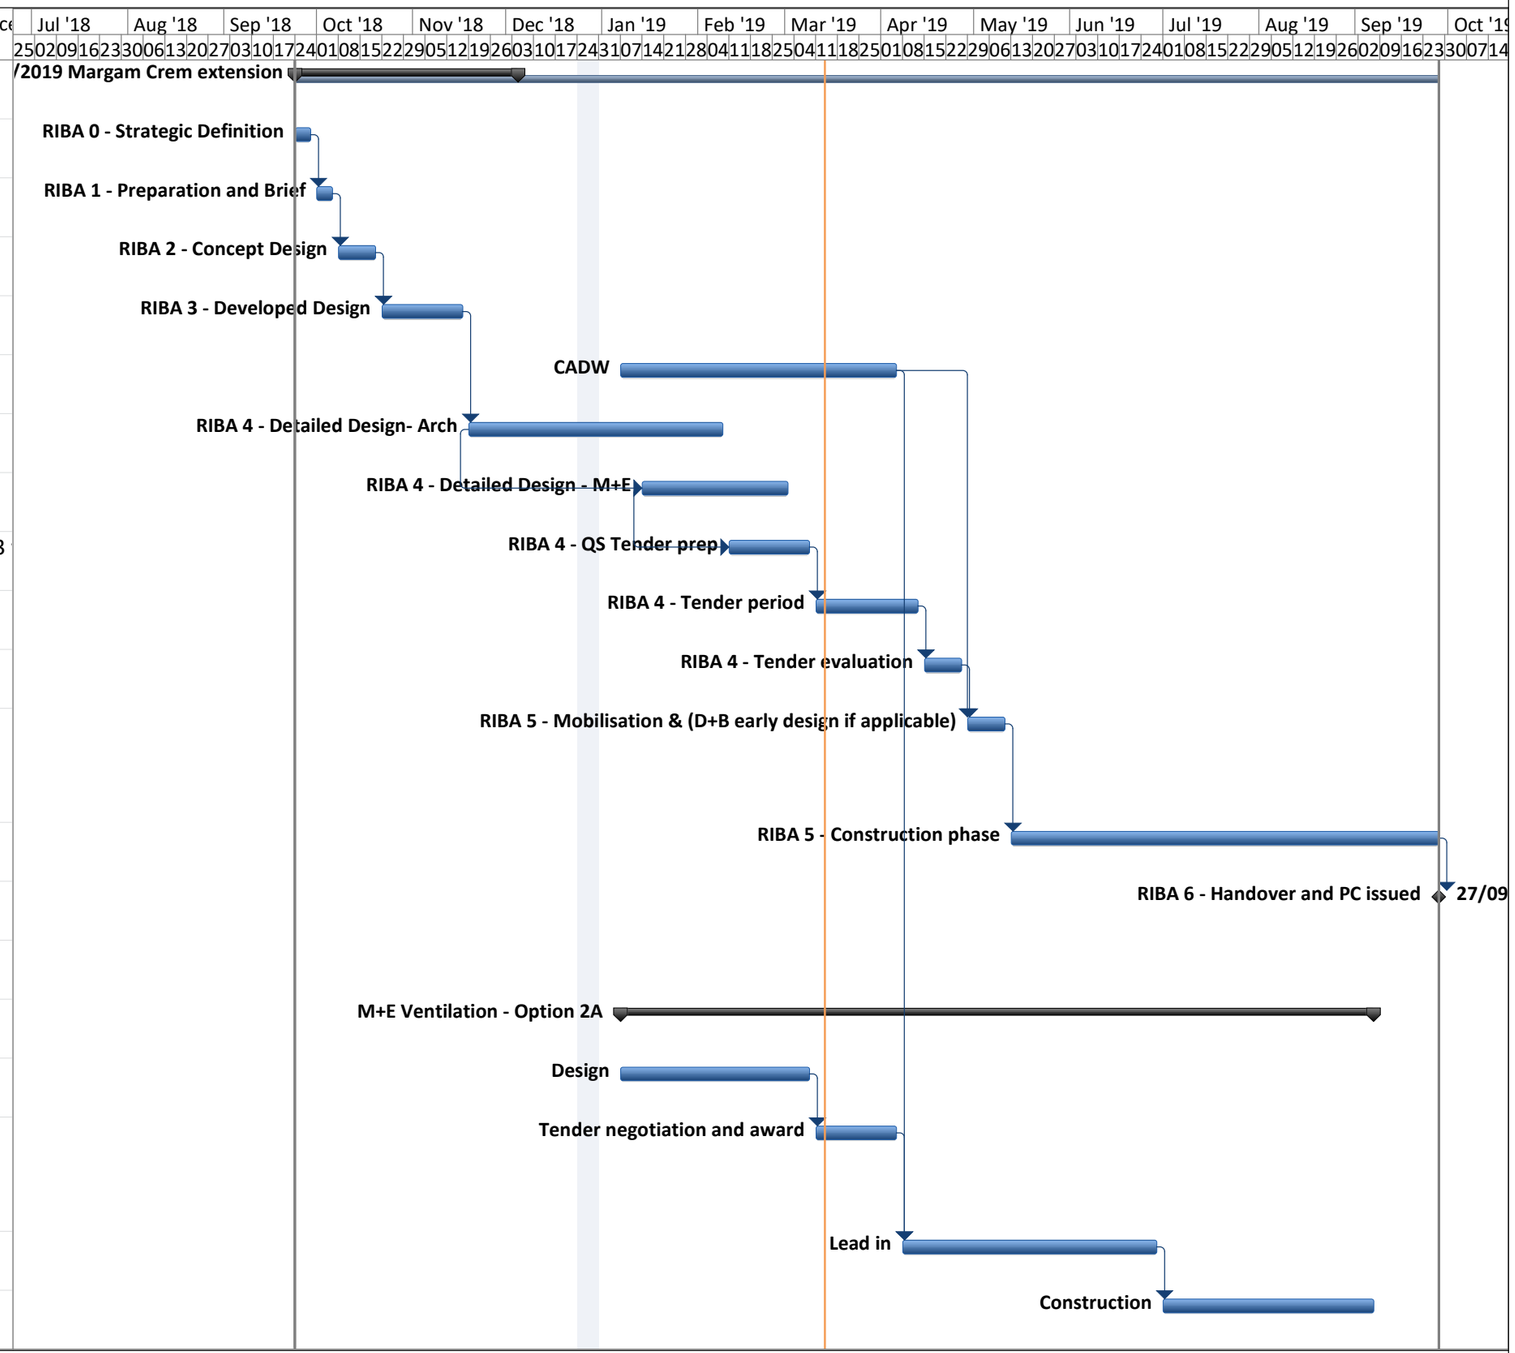

Project: Margam Crem Programm
Date: Thu 14/03/19

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			
